

Agenda Request Form

Cherokee County School District

Meeting Date
May 16, 2019

Agenda Item Number
F-1

Title
Monthly Update on Capital Outlay Projects
Requested Action
School Board Consideration of Superintendent's Recommendation for Approval of the Monthly Update on Capital Outlay Projects
Summary Explanation and Background
See the attached report from the Chief Support Services Officer regarding the status of the current Capital Outlay Projects.
Major System Priority
Increasing Accountability
Financial Impact
N/A
Exhibits: (List)
See Attachment

Board Action
<i>(For Official School Board Records Only)</i>

Source of Additional Information	
William J. Sebring	770.479.1871
Phil Parrott	770.479.1871
Steve Werner	770.479.1871

OFFICE OF THE SUPERINTENDENT OF SCHOOLS

Approved in Open Board Meeting on: _____
(Date)

By: _____
(School Board Chairman)



DATE: 7 May 2019
TO: Dr. Brian V. Hightower
Superintendent of Schools
FROM: William J. Sebring
Chief Support Services Officer
SUBJECT: Construction Status Reports

Facility Construction staff has reviewed the architect's monthly status report on the current construction projects. A summary of the progress for each project is shown below:

Mill Creek Middle School Classroom Addition

- Overhead plumbing and electrical rough-ins are nearing completion on the upper level.
- Mechanical and electrical rough-ins continue on the mezzanine level.
- Brick installation progressing with brick cleaning underway.
- Metal roof panel installation is ongoing and nearing completion.
- Aluminum window installation is underway.
- Planning in progress for tie-in to the existing building over the summer break.
- Preparing for the start of painting activities.
- This project is scheduled for completion August 2020.

A handwritten signature in black ink, appearing to read 'WJ Sebring', written over a horizontal line.

WJS

WJS:dm



Womack Lewis & Smith Inc

Mill Creek Middle School

Print #190427111

Date: 04/27/19


Lat/Lon: 34.117435 -84.477930

Order No. 65859

 **Aerial Photography, Inc.** 954-568-0484



Family and Consumer Science

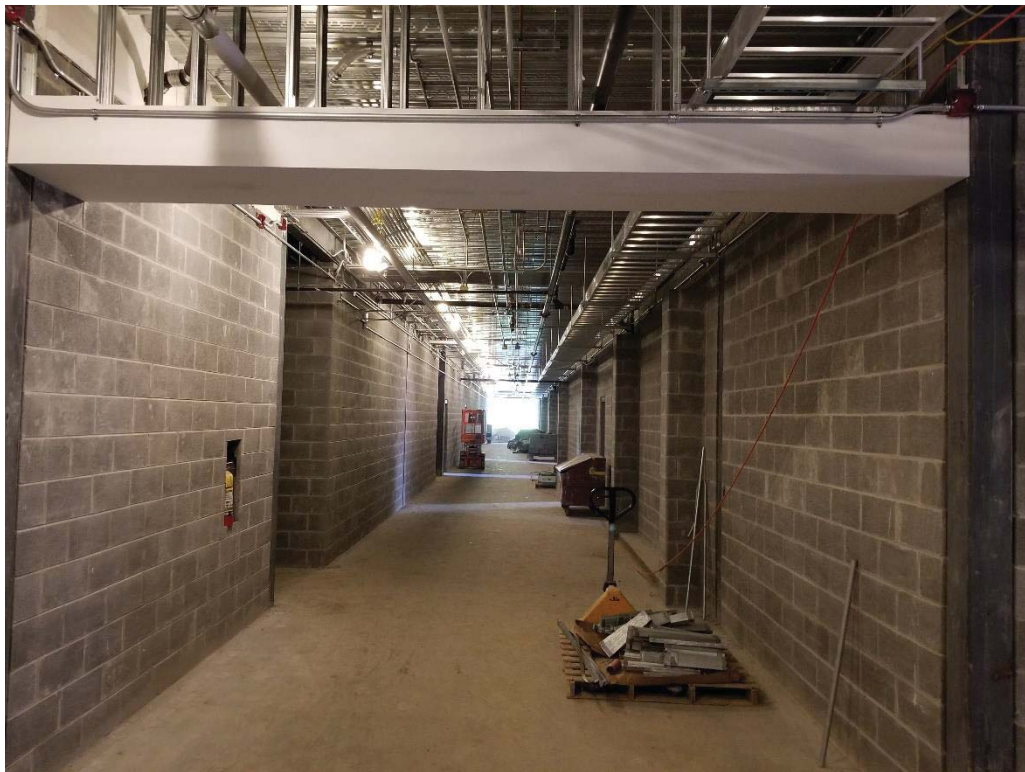

Typical Corridor
